

**RESICOM, INC.**

RESIDENTIAL / COMMERCIAL  
CONSTRUCTION / DESIGN BUILD / MANAGEMENT

---

**SUBMITTAL REVIEW  
CITY OF HOUSTON**

Submittal #: 35

Spec. Section: 01326

Title: Construction Schedule

Description: Construction Schedule

**Water Line Replacement in Tall Timbers Area**

PROJECT NO.: WBS NO.: S-000035-0183-4

ENGINEER: Cobb Fendley

**REVIEWED FOR COMPLIANCE WITH THE CONTRACT DOCUMENTS**

---

DATE: July 17, 2017

*Mashid Ahmadi*

REVIEWED BY



COH--WATER LINE REPLACEMENT IN TALL TIMBERS AREA--WBS #S-000035-0183-4


RESIOCM, INC.

ID	Task Name	Duration	Start	Finish	Jul 16, '17	Jul 23, '17	Jul 30, '17	Aug 6, '17	Aug 13, '17	Aug 20, '17	Aug 27, '17	Sep 3, '17	Sep 10, '17	Sep 17, '17	Sep 24, '17	Oct 1, '17	Oct 8, '17	Oct 15, '17	Oct 22, '17	Oct 29, '17	Nov 5, '17	Nov 12, '17	Nov 19, '17	Nov 26, '17	Dec 3, '17	
62	Service Connection	10 days	Tue 1/23/18	Thu 2/1/18																						
63	Restoration	14 days	Tue 2/6/18	Mon 2/19/18																						
64	<b>EXHIBIT "J"</b>	49 days	Fri 1/12/18	Thu 3/1/18																						
65	Inverness Dr.--Sta. 0+00 to 23+00	11 days	Fri 1/12/18	Mon 1/22/18																						
66	Chlorination/Pressure Test	10 days	Tue 1/23/18	Thu 2/1/18																						
67	Service Connection	8 days	Fri 2/2/18	Fri 2/9/18																						
68	Restoration	10 days	Tue 2/20/18	Thu 3/1/18																						
69	<b>EXHIBIT "K"</b>	52 days	Tue 1/23/18	Thu 3/15/18																						
70	Inverness Dr.(NW)--Sta. 0+80 to 6+80	13 days	Tue 1/23/18	Sun 2/4/18																						
71	Chlorination/Pressure Test	10 days	Mon 2/5/18	Wed 2/14/18																						
72	Service Connection	7 days	Thu 2/15/18	Wed 2/21/18																						
73	Restoration	14 days	Fri 3/2/18	Thu 3/15/18																						
74	<b>EXHIBIT "L"</b>	56 days	Mon 2/5/18	Sun 4/1/18																						
75	Inverness Dr.--Sta. 23+00 to 43+40	10 days	Mon 2/5/18	Wed 2/14/18																						
76	Willowick St.--Sta. 19+00 to 26+00	7 days	Thu 2/15/18	Wed 2/21/18																						
77	Chlorination/Pressure Test	11 days	Thu 2/22/18	Sun 3/4/18																						
78	Service Connection	14 days	Mon 3/5/18	Sun 3/18/18																						
79	Restoration	14 days	Mon 3/19/18	Sun 4/1/18																						
80	<b>EXHIBIT "M"</b>	53 days	Thu 2/22/18	Sun 4/15/18																						
81	Knollwood Dr.--Sta. 0+20 to 17+25	7 days	Thu 2/22/18	Wed 2/28/18																						
82	Timber Lane--Sta. 19+40 to 24+10	4 days	Thu 3/1/18	Sun 3/4/18																						
83	Willowick St.--Sta. 53+20 to 57+40	4 days	Mon 3/5/18	Thu 3/8/18																						
84	Chlorination/Pressure Test	10 days	Fri 3/9/18	Sun 3/18/18																						
85	Service Connection	8 days	Mon 3/19/18	Mon 3/26/18																						
86	Restoration	14 days	Mon 4/2/18	Sun 4/15/18																						
87	<b>EXHIBIT "N"</b>	52 days	Fri 3/9/18	Sun 4/29/18																						
88	Willowick St.--Sta. 26+00 to 53+20	17 days	Fri 3/9/18	Sun 3/25/18																						
89	Chlorination/Pressure Test	10 days	Mon 3/26/18	Wed 4/4/18																						
90	Service Connection	9 days	Thu 4/5/18	Fri 4/13/18																						
91	Restoration	14 days	Mon 4/16/18	Sun 4/29/18																						
92	<b>EXHIBIT "O" &amp; "P"</b>	66 days	Mon 3/26/18	Wed 5/30/18																						
93	Pinehill Ln. Sanitary Sewer--Sta. 0+84 to 8+20	14 days	Mon 3/26/18	Sun 4/8/18																						
94	Pressure Test Sewer Line	7 days	Mon 4/9/18	Sun 4/15/18																						
95	Pinehill Ln. Water Line--Sta. 0+70 to 9+00	7 days	Mon 4/16/18	Sun 4/22/18																						
96	Chlorination/Pressure Test	10 days	Mon 4/23/18	Wed 5/2/18																						
97	Service Connection	14 days	Thu 5/3/18	Wed 5/16/18																						
98	Restoration	14 days	Thu 5/17/18	Wed 5/30/18																						
99	Wet Connects & Cut/Plugs	21 days	Thu 5/17/18	Wed 6/6/18																						
100	<b>FINAL RESTORATION</b>	14 days	Thu 6/7/18	Wed 6/20/18																						
101	<b>FINAL CLEAN-UP</b>	12 days	Thu 6/21/18	Mon 7/2/18																						
102	<b>SUBSTANTIAL COMPLETION</b>	0 days	Mon 7/2/18	Mon 7/2/18																						

WATER LINE REPLACEMENT  
IN TALL TIMBERS AREA  
Date: Mon 7/17/17

Task Split Milestone Summary Project Summary Finish-only Progress

Dec 10, '17 Dec 17, '17 Dec 24, '17 Dec 31, '17 Jan 7, '18 Jan 14, '18 Jan 21, '18 Jan 28, '18 Feb 4, '18 Feb 11, '18 Feb 18, '18 Feb 25, '18 Mar 4, '18 Mar 11, '18 Mar 18, '18 Mar 25, '18 Apr 1, '18 Apr 8, '18 Apr 15, '18 Apr 22, '18 Apr 29, '18 May 6, '18 May 13, '18 May 20, '18 May 27, '18 Jun 3, '18 Jun 10, '18 Jun 17, '18 Jun 24, '18 Jul 1, '18 Jul 8, '18

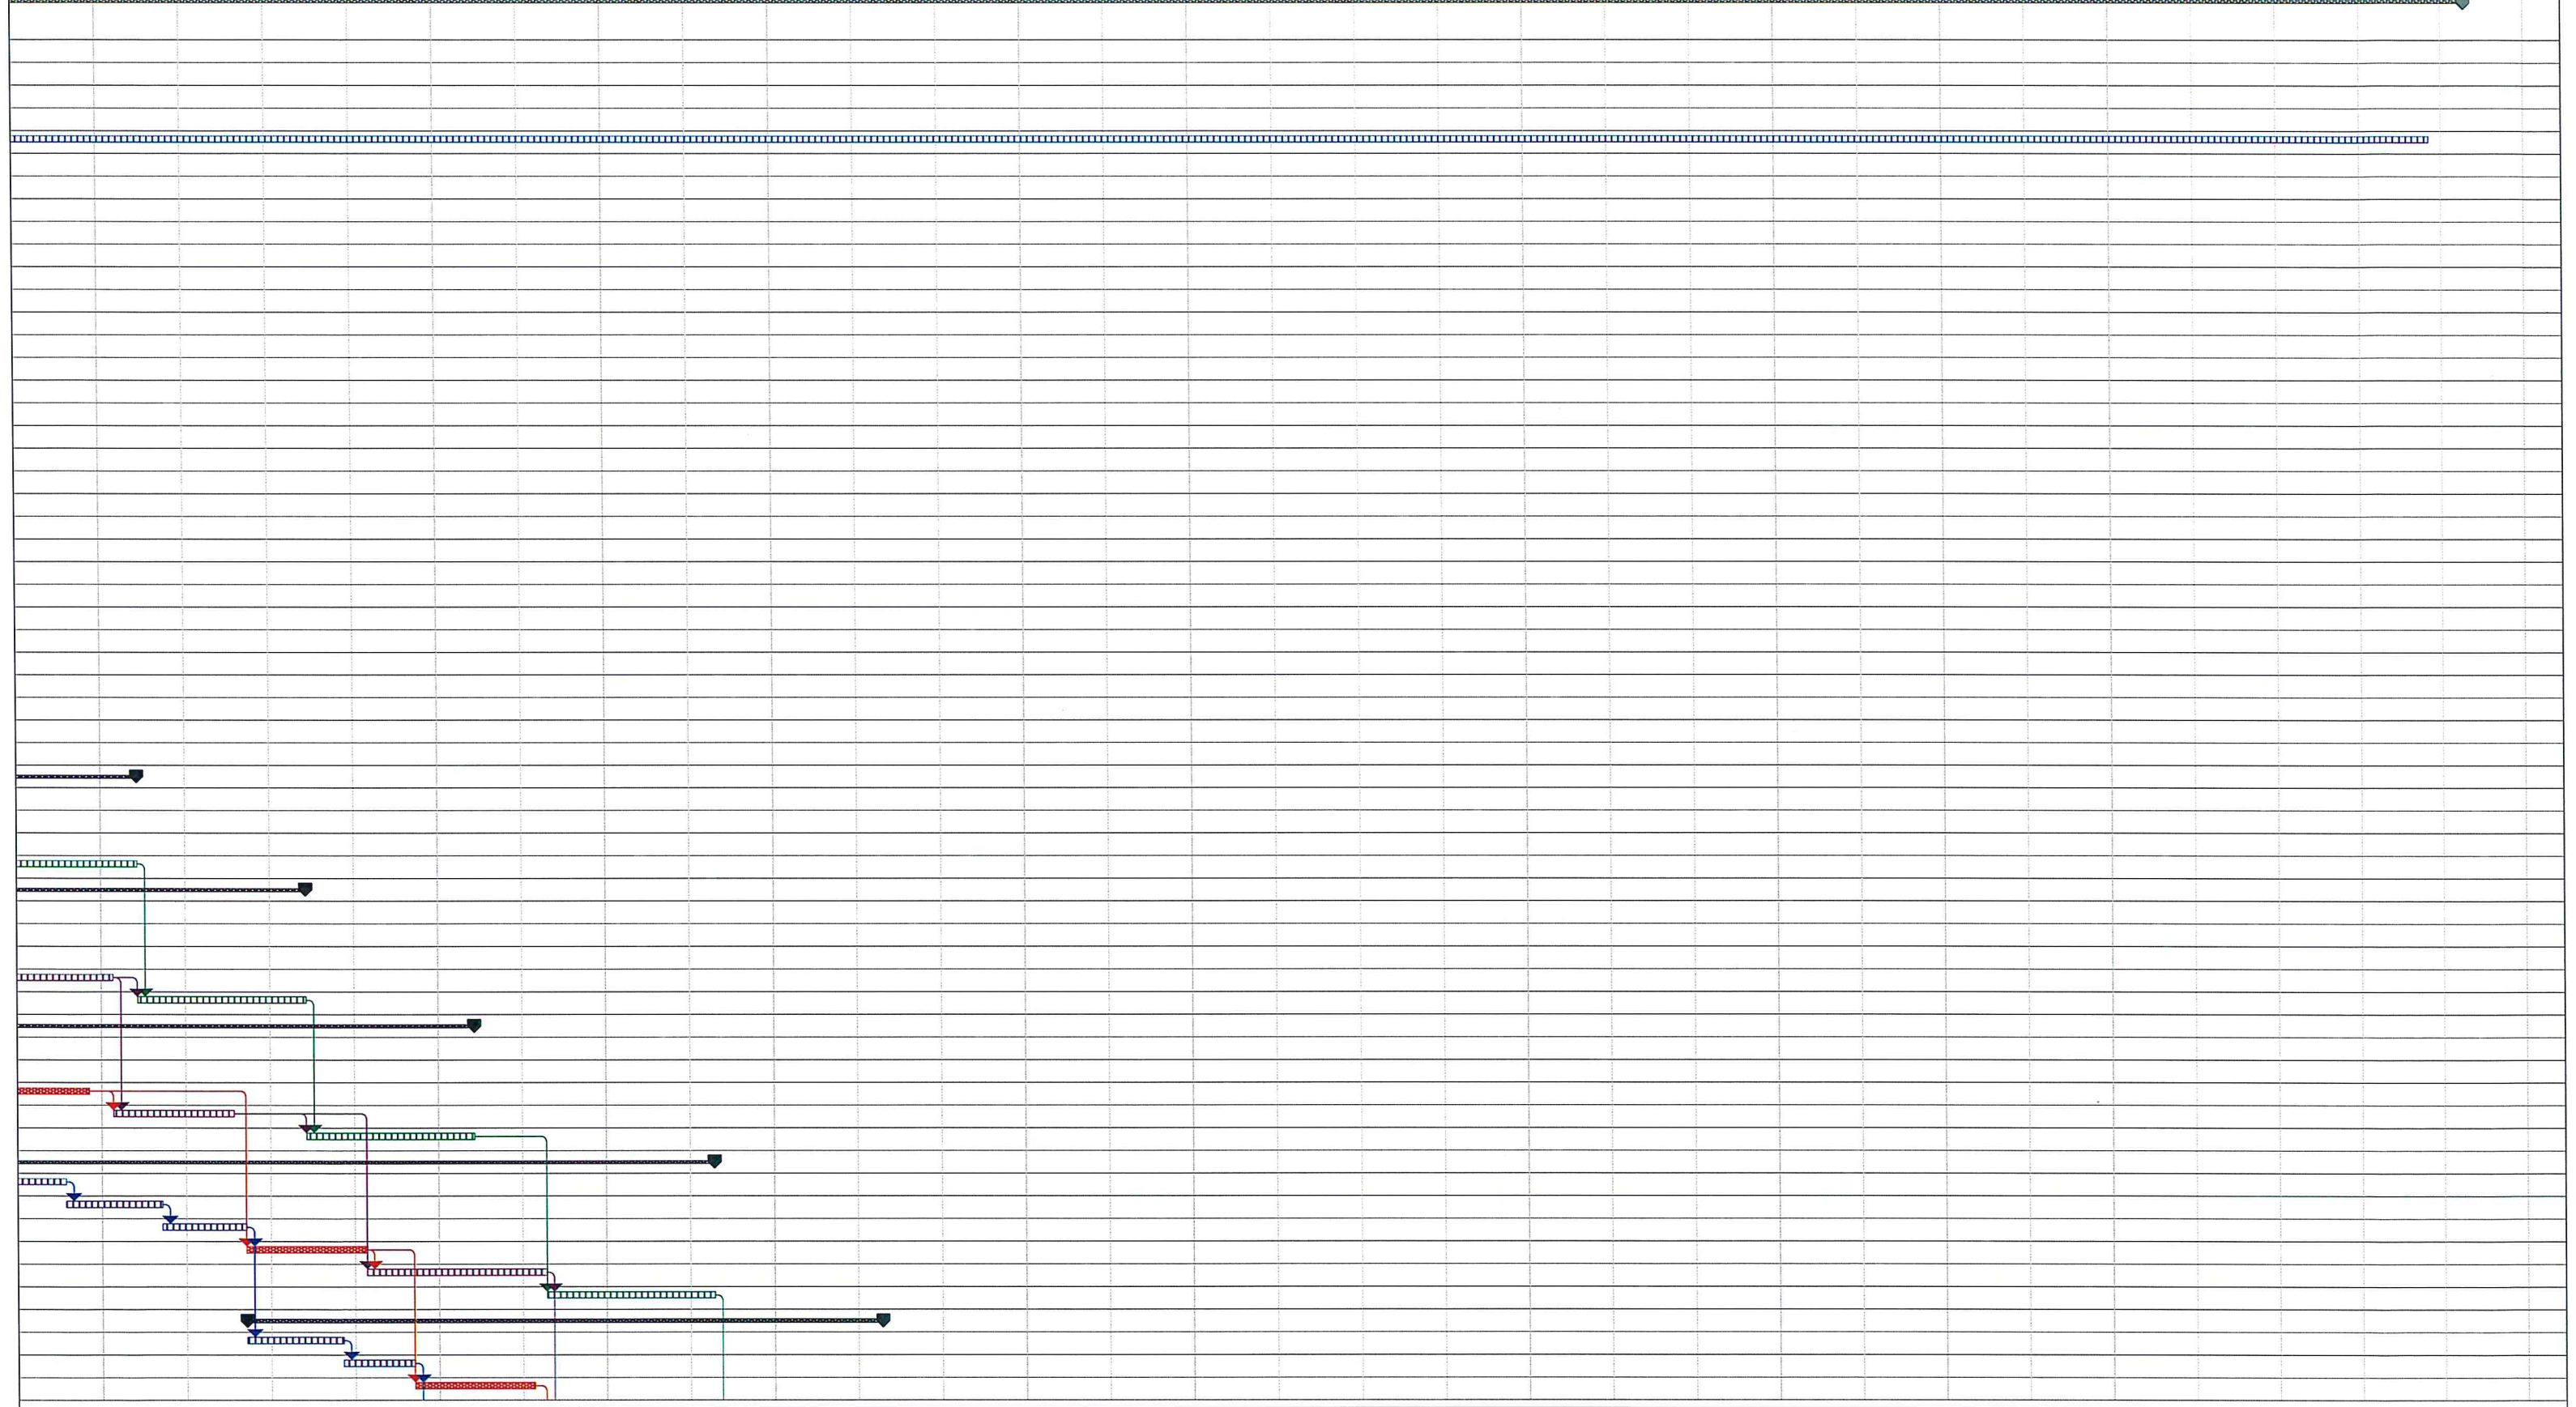

**WATER LINE REPLACEMENT  
IN TALL TIMBERS AREA**  
Date: Mon 7/17/17

Task      Split      Milestone      Summary      Project Summary      Finish-only      Progress

COH--WATER LINE REPLACEMENT IN TALL TIMBERS AREA--WBS #S-000035-0183-4

RESIOCM, INC.

Dec 10, '17 Dec 17, '17 Dec 24, '17 Dec 31, '17 Jan 7, '18 Jan 14, '18 Jan 21, '18 Jan 28, '18 Feb 4, '18 Feb 11, '18 Feb 18, '18 Feb 25, '18 Mar 4, '18 Mar 11, '18 Mar 18, '18 Mar 25, '18 Apr 1, '18 Apr 8, '18 Apr 15, '18 Apr 22, '18 Apr 29, '18 May 6, '18 May 13, '18 May 20, '18 May 27, '18 Jun 3, '18 Jun 10, '18 Jun 17, '18 Jun 24, '18 Jul 1, '18 Jul 8, '18

